City of Salinas - Fiber Extension to 312 E. Alisal

Preliminary Schedule Study

Updated 08.17.18
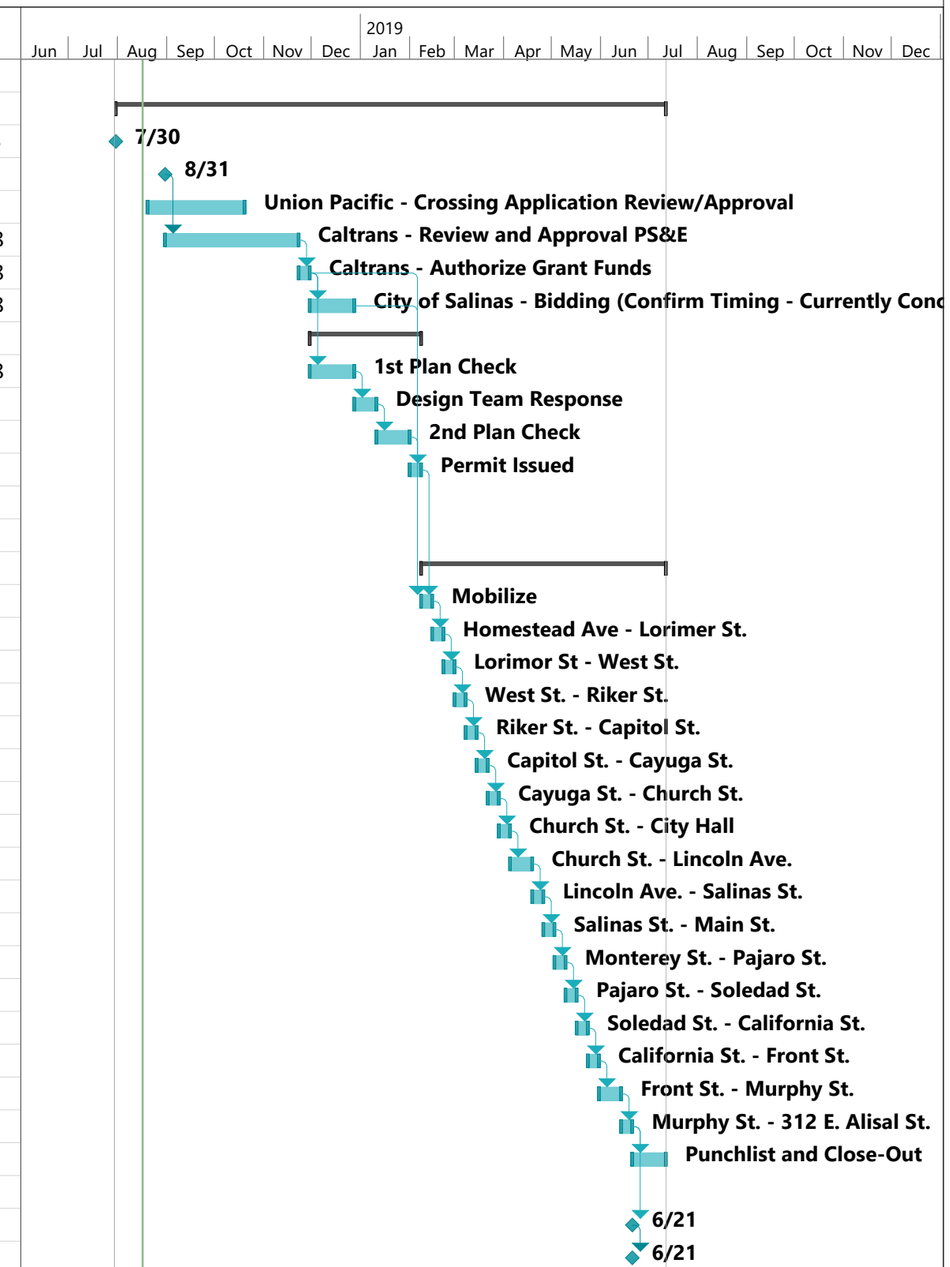
ID	Task Name	Duration	Start	Finish
1				
2	**Fiber Extension to SPSH**	**248 days**	**Mon 7/30/18**	**Thu 7/11/19**
3	City of Salinas - Review and Compile Comments to incorporate into Final Plans	0 days	Mon 7/30/18	Mon 7/30/18
4	City of Salinas - Receive Final Plans	0 days	Fri 8/31/18	Fri 8/31/18
5	Union Pacific - Crossing Application Review/Approval	9 wks	Mon 8/20/18	Fri 10/19/18
6	Caltrans - Review and Approval PS&E	3 mons	Fri 8/31/18	Thu 11/22/18
7	Caltrans - Authorize Grant Funds	1 wk	Fri 11/23/18	Thu 11/29/18
8	City of Salinas - Bidding (Confirm Timing - Currently Concurrent with Permitting)	1 mon	Fri 11/30/18	Thu 12/27/18
9	**City of Salinas - Permitting Process**	**50 days**	**Fri 11/30/18**	**Thu 2/7/19**
10	1st Plan Check	4 wks	Fri 11/30/18	Thu 12/27/18
11	Design Team Response	2 wks	Fri 12/28/18	Thu 1/10/19
12	2nd Plan Check	3 wks	Fri 1/11/19	Thu 1/31/19
13	Permit Issued	1 wk	Fri 2/1/19	Thu 2/7/19
14				
15				
16	**Construction**	**110 days**	**Fri 2/8/19**	**Thu 7/11/19**
17	Mobilize	1 wk	Fri 2/8/19	Thu 2/14/19
18	Homestead Ave - Lorimer St.	1 wk	Fri 2/15/19	Thu 2/21/19
19	Lorimor St - West St.	1 wk	Fri 2/22/19	Thu 2/28/19
20	West St. - Riker St.	1 wk	Fri 3/1/19	Thu 3/7/19
21	Riker St. - Capitol St.	1 wk	Fri 3/8/19	Thu 3/14/19
22	Capitol St. - Cayuga St.	1 wk	Fri 3/15/19	Thu 3/21/19
23	Cayuga St. - Church St.	1 wk	Fri 3/22/19	Thu 3/28/19
24	Church St. - City Hall	1 wk	Fri 3/29/19	Thu 4/4/19
25	Church St. - Lincoln Ave.	2 wks	Fri 4/5/19	Thu 4/18/19
26	Lincoln Ave. - Salinas St.	1 wk	Fri 4/19/19	Thu 4/25/19
27	Salinas St. - Main St.	1 wk	Fri 4/26/19	Thu 5/2/19
28	Monterey St. - Pajaro St.	1 wk	Fri 5/3/19	Thu 5/9/19
29	Pajaro St. - Soledad St.	1 wk	Fri 5/10/19	Thu 5/16/19
30	Soledad St. - California St.	1 wk	Fri 5/17/19	Thu 5/23/19
31	California St. - Front St.	1 wk	Fri 5/24/19	Thu 5/30/19
32	Front St. - Murphy St.	2 wks	Fri 5/31/19	Thu 6/13/19
33	Murphy St. - 312 E. Alisal St.	1 wk	Fri 6/14/19	Thu 6/20/19
34	Punchlist and Close-Out	3 wks	Fri 6/21/19	Thu 7/11/19
35				
36	Fiber Installation Complete to 312 E. Alisal	0 days	Fri 6/21/19	Fri 6/21/19
37	Network activated ???	0 days	Fri 6/21/19	Fri 6/21/19
